ENGINEERING PLANS — AMENDMENTS

Casa Abadia · Praceta da Abadia, Lote 13 · Ericeira, Mafra

Rev. 2 · 26 August 2026 · Owner: Sébastien Maillard / Natasha Santric

Four amendments to the engineering designs of July 2026 (GAP LR, process 3775). Each is to be re-engineered and priced by the responsible contractor.

WOOD-HOME ELECTRICIAN GONÇALO AVAC / GAP LR OTK

Please confirm per item: technical solution, cost impact, and the construction stage by which it must be fixed.

1. Closet — ventilation and climate

WOOD-HOME AVAC / GAP LR ELECTRICIAN


Ref: AVAC, drawing 03 — Planta do Piso 1, Ventilação

Goal. The 1st floor walk-in closet (9.30 m²) to be served by the AC and VMC systems. It is not on the current drawing.

Main points

- **Wood-Home:** duct openings through the structural panels to be made in the factory, not cut on site.
- Extraction is the priority — humidity and odour control.
- An air return path is needed (door undercut or transfer grille).
- Confirm the impact on the thermal calculation and on heat pump sizing.
- Duct routing to be coordinated with the closet joinery before manufacture.

Required by: Before the structural panels and closet joinery are manufactured.

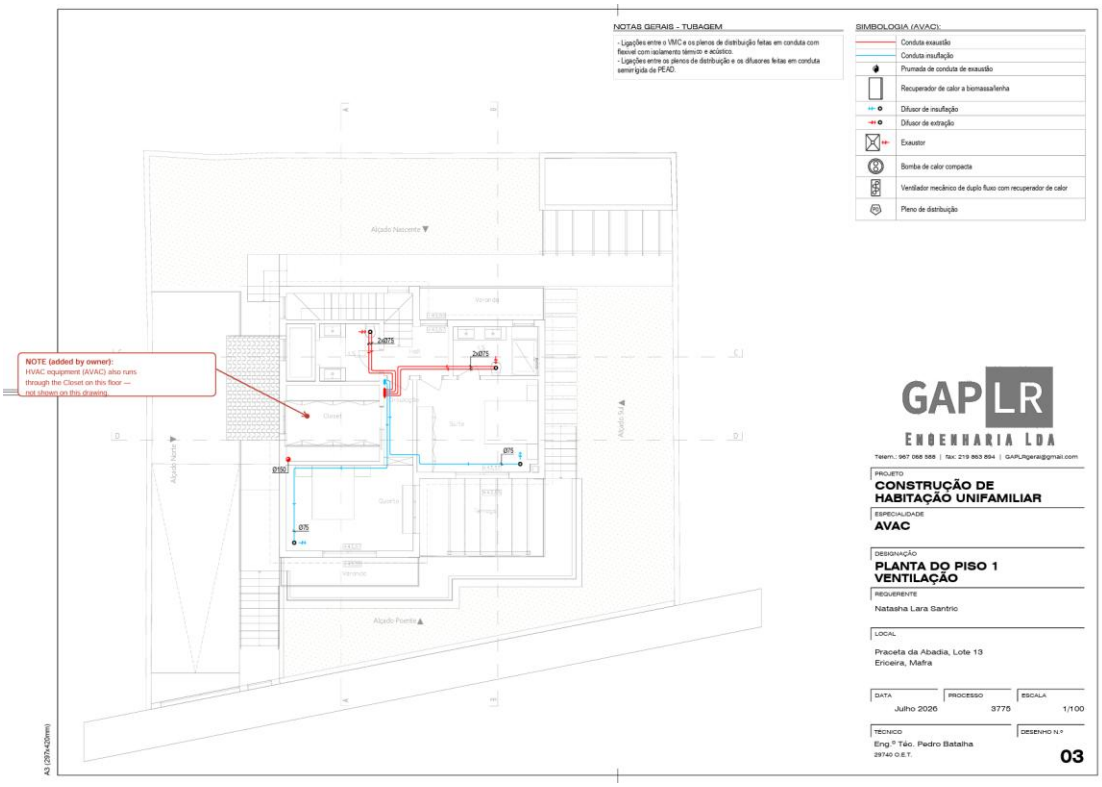

2. Basement — drainage for a future tap and shower

GONÇALO AVAC / GAP LR


Ref: Rede de Águas Residuais, drawing 02 — Planta do Piso -1

Goal. Leave capped waste and water connections in the basement so a tap and shower can be added later without breaking the slab.

Main points

- Connect into the existing inspection chamber (marked on the drawing).
- **Critical —** confirm there is enough fall for a shower trap: basement floor is at +37.50, the existing connection invert at 37.20. If gravity is insufficient, provide a pumping chamber.
- Include venting; a trap without a vent will siphon.
- Add cold and hot water stubs in the same operation.
- Stub-outs to be capped, photographed and their positions recorded before the pour.

Required by: Before the foundation slab is poured. This item cannot be recovered later.

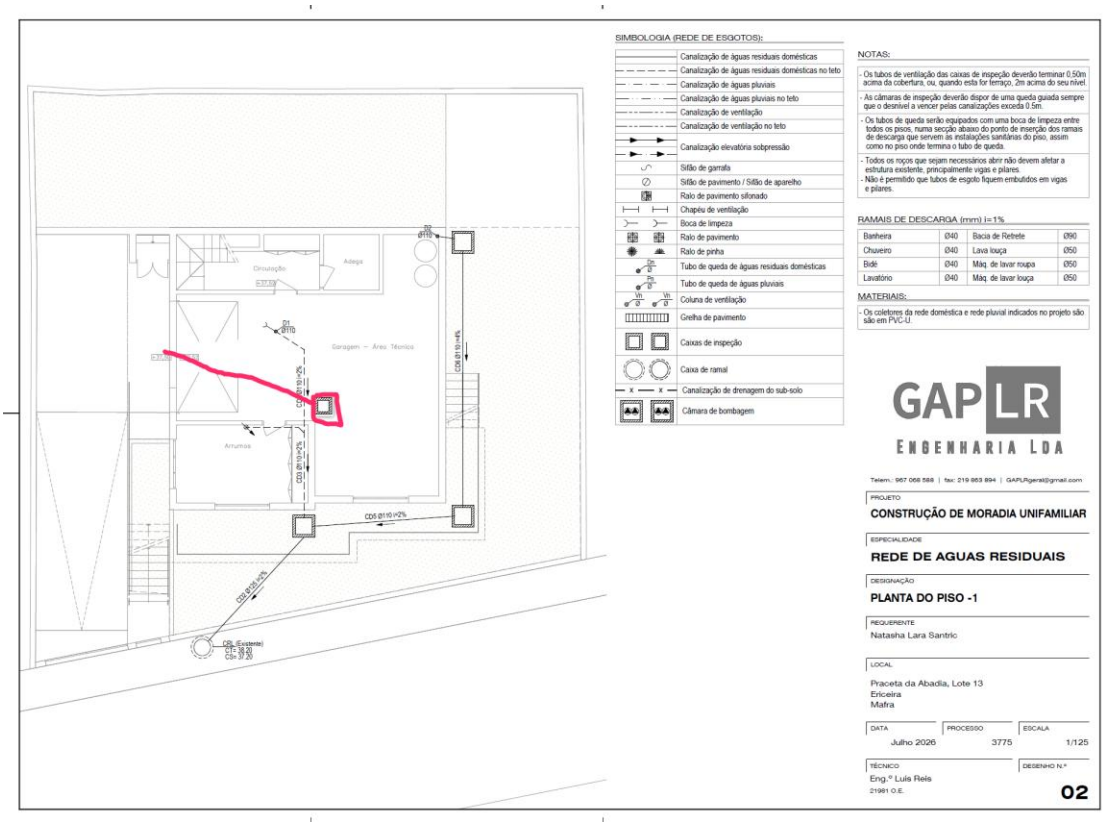

3. Photovoltaic — pre-installation

WOOD-HOME ELECTRICIAN


Ref: Planta da Cobertura — to be marked on the electrical drawing (IE), not ITED

Goal. Roof and electrical installation prepared for a future PV system, so that fitting it later requires no work on the sealed roof or the finished walls.

Main points

- **Pitched roof —** the array goes on the south-facing plane only.
- Initial target ~9 m² (≈ 2 kWp). Size the provision for expansion to about 5 kWp — extra provision now costs very little.
- **Wood-Home:** structural anchors and waterproofed penetrations built into the roof panels in the factory; confirm the additional load is covered by the structural design.
- **Electrician:** DC conduit roof → technical room, separate from AC and ITED; reserved breaker space in the board; inverter and battery position; earthing and bonding.
- Panel layout to be proposed by the contractor.

Required by: Before the roof panels are manufactured.

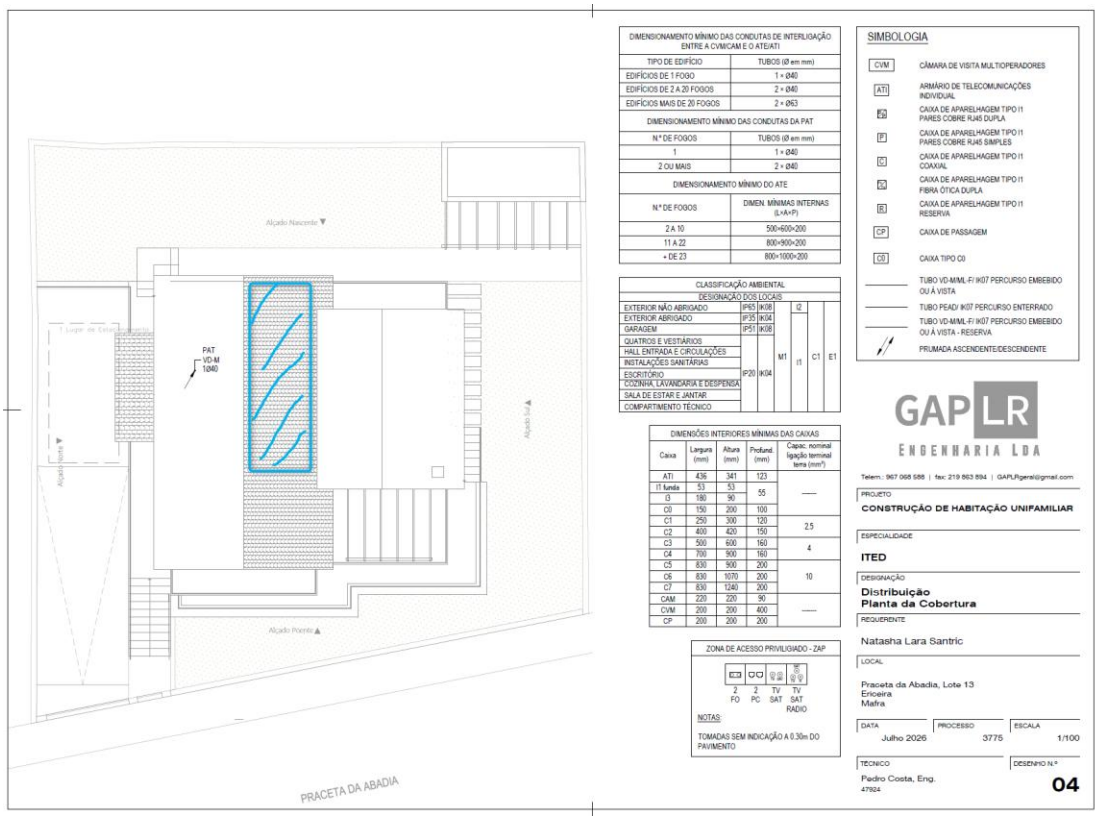

4. First floor — terrace extension

WOOD-HOME

Ref: Planta do Piso 1

Goal. Extend the 1st floor terrace so it is possible to walk between the two bedroom terraces (see mark).

Main points

- **OTK has confirmed** the extension is acceptable within the approved design — no licensing amendment required.
- Minimum clear passage width to be confirmed — target 1.00 m.
- Includes structure, continuity of the waterproofing, guardrail, and a rainwater drain point for the added area.

Required by: Before the 1st floor panels are manufactured.

