WOOD HOME

YOUR PREFABRICATED WOODEN HOME



Offer no 26244v6

03.09.2026

"Wood–Home", SL&S AG, Słoneczna 50, 40–136 Katowice NIP 6322009926

How can we help you?

Custom Designs

We design your home from the ground up—perfectly tailored to your needs, lifestyle, and plot.

Ready-Made Designs

If time is of the essence, our portfolio includes a selection of ready-made designs. We also adapt pre-designed or custom projects from external architectural firms.

Your Trusted Partner

Holding the German BMF-RAL quality certification and roots dating to 1979, we are a partner you can rely on. We build across Europe, drawing on extensive expertise gained primarily in the demanding German and Austrian markets. Our track record encompasses single and multi-family homes, real estate developments, and public buildings.

In-House Prefabrication

We have been manufacturing ready-to-build homes for over 20 years. Prefabrication ensures superior quality through rigorous Factory Production Control—a standard unattainable with traditional building methods.

High-Tech Prefabrication

The ready components of your home are manufactured in advance at our facility—pre-plastered and fully insulated. Windows and doors are pre-installed in a secure, airtight, and energy-efficient manner.

Construction Time

The assembly of a single-family home typically takes just 3 to 6 days, including the roof covering! This remarkable speed is made possible by our prefabrication process.

Price Guarantee

Our advanced design process and stable production environment keep your budget safely under control. The price agreed upon at the start remains fixed throughout construction. There are no hidden costs or unexpected surcharges.

Durability and Safety


We have been building homes for years using proven materials and technologies. We consistently achieve excellent results in airtightness tests (Blower Door Test). We are a certified BMF-RAL manufacturer and a member of SEDG.

End-to-End Project Support

We guide you through the entire process—from your first decisions to the final completion of the build. You maintain constant contact with your dedicated Project Manager, receiving clear information at every stage. No guesswork, no searching for answers on your own.

Technology and Materials

We build our homes using high-quality materials from trusted manufacturers!

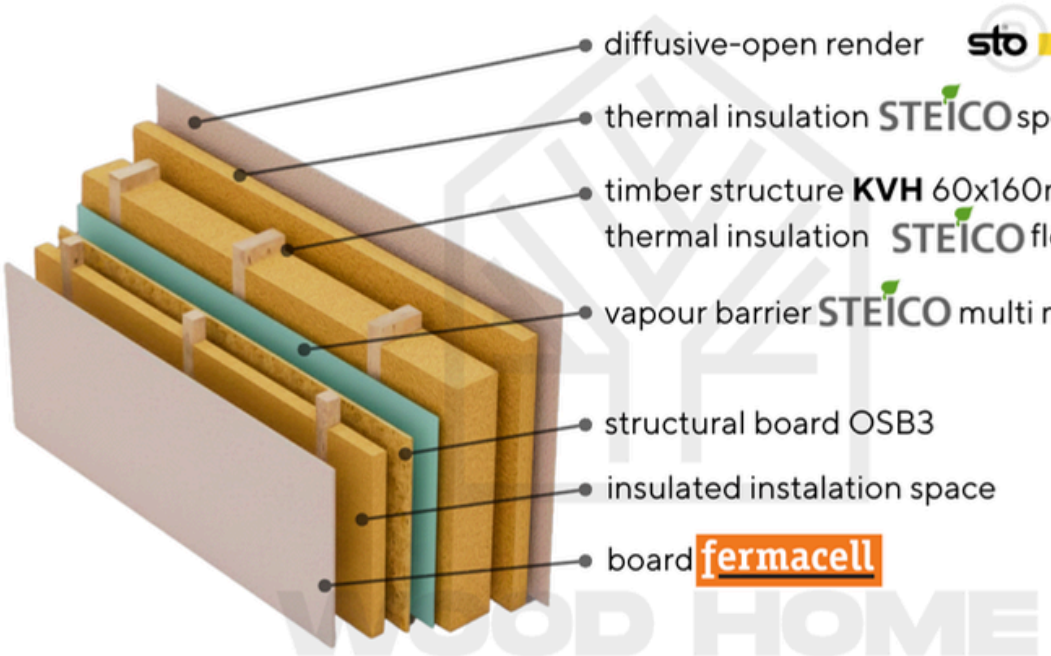

U=0,15 $\frac{W}{m^2K}$
t=15,2h



STEICO A comprehensive building system based on STEICO wood wool guarantees the best thermal insulation properties, ensuring low heating bills in the winter and reduced cooling costs in the summer.
This eco-friendly, vapour-permeable insulation system simultaneously ensures the durability of the entire building envelope.
STEICO wood wool is your guarantee of a warm, healthy, ecological, and energy-efficient home.


STO Render & Vapour Permeability

sto



The exterior walls are finished with a vapour-permeable render by STO, which guarantees a failure-free facade.
The external building envelope is designed as a vapour-permeable structure, allowing water vapour to naturally migrate outwards. This ensures the longevity of your home and a healthy indoor microclimate.

Structural Timber



Let's not forget about the wood! At Wood-Home, we use exclusively certified KVH and C24 timber. It is kiln-dried, planed, and features chamfered edges—your guarantee of a robust and long-lasting structure.



Fermacell Interior Boards

All interior walls are finished with fermacell boards. They are ready for filling and painting, with no need for additional interior plastering! You can hang weights of up to 50kg on a single wall plug, anywhere on the fermacell boards! This guarantees ease of use, lasting durability, and everyday safety.

Building process









design → production → foundation → assembly → other works












About design



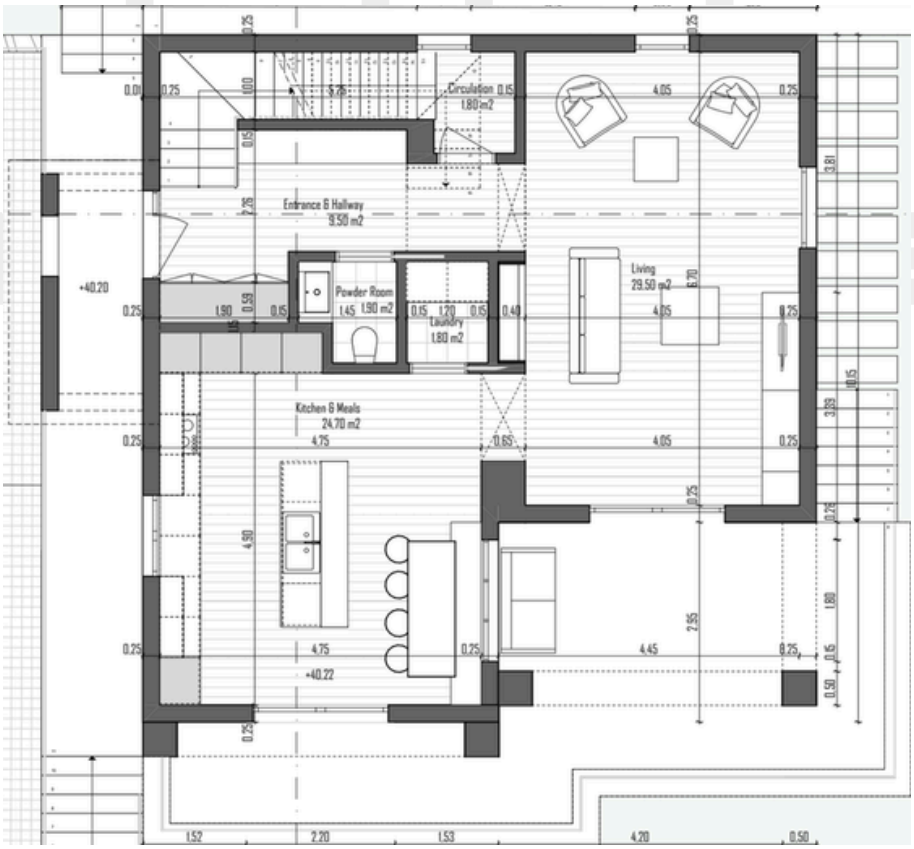

Scope of work 1/2

1. Design Works

- Structural engineering design,
- Shop drawings for prefabricated elements,
- Complete as-built documentation.

2. Construction Works

Roof:

- ~~Complete roof covering with Braas ceramic roof tiles + sheet metal flashings, color~~ ....., on a substructure of battens and counter-battens,
- Installation of a complete steel guttering system down to ground level (level "zero"), color ……..…,
- Premium breather membrane (wind barrier) Dorken Universal XX,
- Structure made of certified KVH timber (cross-section according to the structural engineering design),

External walls (U-value = 0.17):

- Plastered facade, STO plaster system, diffusion-open system, without the final decorative plaster finish,
- STEICOspecial dry 60mm wood fiber facade board,
- KVH structural timber framework 60x120 insulated with STEICOflex 036 wood fiber insulation,
- 12.5mm Fermacell board,
- STEICOmulti renova vapor barrier membrane,
- Service cavity on a wooden frame, insulated with STEICOflex 036 50mm,
- 12.5mm Fermacell board,
- Horizontal damp-proof course (DPC) beneath the ground floor walls,
- Perimeter damp-proof sealing between the building and the foundation using EPDM membrane,
- Corrugated conduits pre-installed in the walls for electrical wiring, with pre-cut holes for socket and switch back-boxes.

Internal wall:

- 12.5mm Fermacell board,
- KVH structural timber framework 60x120 insulated with 80mm thick STEICOflex 036 wood fiber insulation,
- 12.5mm Fermacell board.

Floor / Ceiling structure:

- OSB3 22mm structural board,
- Structure made of certified KVH timber (cross-section according to the structural engineering design),

Flat roof (Balcony):

- H20 fermacell board
- OSB3 25mm structural board,
- KVH roof joists, cross-section as per structural calculations,
- fermacell board + STO plaster system

Scope of work 2/2

Window and Door Joinery:

- Installed Salamander Prestige bE82/MD PVC windows (3 gaskets, triple glazing, RAL-compliant warm installation, multi-functional expanding joint sealing tapes, 6-chamber profile, Uw-value from 0.74 W/m^2K, Ug-value = 0.5 W/m^2K) in color ……., including an HST (lift-and-slide) door (4 pcs.), with tint,
- Installed energy-efficient wooden entry door Doorsy Meduno (Standard II: 100 mm thick door leaf with a gasket), 100 mm wide fixed door frame with a gasket, quadruple-glazed, three-chamber unit with one-way mirror glass, four 3D-adjustable hinges by the Swiss company SFS with anti-tamper protection and decorative caps, standard color: ……, RAL-compliant warm installation, with a sidelight,
- Motorized Aluprof external roller shutters, on 2 HST and 1 side window,
- Within the 3 windows with shutter: sliding mosquito doors,
- Installed aluminum external window sills in color ..... according to RAL guidelines, mounted on a secondary sealing layer, with a minimum overhang of 40mm

Additionally included in the price:

- Transport to the construction site,
- Complete set of fasteners and hardware for assembly,
- Building assembly / installation,
- Fakro loft ladder (attic stairs),
- Schiedel prefabricated chimney system,
- Wooden eaves soffit, painted twice with Flugger Woodtex,
- Visible wooden elements painted with the Flugger system (1x primer + 2x wood stain),
- Temporary site staircase,
- Arches: STEICOspecial dry + STO plaster system,
- Wooden pergola over the balcony,
- Termite protection - mesh barrier,

Summary:

- Building weather-tight and secured from the outside,
- Complete set of windows and doors,
- Interior finished with Fermacell boards,
- Pre-installed corrugated conduits for electrical wiring,
- Transport and assembly – included in the price.

Client's / Investor's Responsibilities:

- Preparation of the foundation,
- Scaffolding for the duration of the assembly,
- Crane for the duration of the assembly,
- Accommodation for the assembly crew (usually 4-5 people for approx. 5 days),
- Site toilet (portable toilet),
- Water and electricity supply for the duration of the assembly,
- Hardened / paved access road to the construction site,
- Other construction works not specifically listed in this offer,

Excluding:

- Excluding railings, stairs, and decorative façade elements (stone, timber, boards).
- Excluding electrical, water, and sewage installations, central heating, ventilation.
- Excluding insulation and concrete screeds / floor slabs.
- Excluding sanitary installations.
- Excluding plasterboard lining to ceilings and roof.

Portfolio

YOUR WOODEN HOME

Custom Designs







Ready-Made Designs






Premium Developments






WOOD HOME®

News

YOUR WOODEN HOME

premium designs






If you have something completely custom in mind and aren't interested in ready-made designs – you have come to the right place. We will gladly design a home for you that is truly "yours" – refined in every detail, thoughtfully planned, and simply unique.

Ask about our premium projects, which are not published on our website.

Collins House & Bombowy Domek

King Casimir the Great at Wood-home



"They found a masonry Poland, and will leave it timber-built!"
Our Vision for Sustainable Construction We believe high-quality timber frame construction is the industry's future—a natural, eco-friendly, and highly durable response to the needs of modern investors.
Commitment to Market Education
We strongly emphasize industry education by demonstrating best building practices and highlighting the crucial structural details required to construct long-lasting, energy-efficient homes.
Our Brand Ambassador
Wood-Home is proudly represented by Greg Collins. In our social media campaigns, he occasionally plays King Casimir the Great to creatively champion the superiority of modern wood construction.

fairs events 2026

You can meet Wood-home at fairs:

- BUDMA fairs, Poznań, February 2026
- International Building Fairs PreZero Arena Gliwice, March 2026
- Building Fairs EXPOBUD Gliwice, September 2026

open days

Next **Open days at Wood-home**:

- Alwernia k. Krakowa
- Ojrzanów k. Nadarzyna
- Nadarzyn
- Cholerzyn k. Krakowa
- Lichnówki k. Tczewa
- Wrocław
- Praga (Czechy)
- Katowice
- Poznań

Ask about next dates!

WOOD HOME®

FAQ

YOUR WOODEN HOME

Standard technologiczny i energooszczędny Wood-home

1. Do Wood-Home houses meet strict energy efficiency standards?
Yes. Our external building envelope achieves an excellent thermal transmittance (U-value) of 0.15 W/m²K. As standard, we install a Panasonic High Performance heat pump and a Thessla Green heat recovery ventilation (HRV) system. This configuration ensures the house is highly energy-efficient and fully prepared for net-zero emission standards.

2. Why do you use the STEICO system, and what are its advantages?
We choose STEICO because it is a comprehensive, eco-friendly insulation system based on wood fiber (STEICOspecial dry boards and STEICOflex 036 insulation). Its primary advantage is a high thermal phase shift, which in our homes reaches up to t = 15.2h. This means it takes over 15 hours for external heat to penetrate the interior. This guarantees low heating bills in winter and effective protection against indoor overheating in summer. Additionally, STEICO materials have a negative carbon footprint, making the house highly sustainable.

3. What does it mean for a wall to be "diffusion-open" (vapor-permeable)?
By utilizing an external STO render system and wood wool insulation, our building envelope allows for the natural outward migration of water vapor. The building "breathes," which ensures a healthy indoor microclimate and guarantees long-term structural durability by completely eliminating the risk of interstitial condensation (moisture buildup) within the framework.

4. What are the interior walls finished with, and why not standard drywall?
All interior walls are finished with Fermacell gypsum fiberboards. They have a significantly higher density than standard plasterboard, which vastly improves acoustic insulation between rooms. Most importantly, they are exceptionally durable—you can hang loads of up to 50 kg on a single wall plug anywhere on the wall, without the need to plan for reinforcing frameworks.

5. Are timber frame houses fire-safe and durable?
For the main load-bearing structure, we exclusively use certified KVH structural timber (e.g., 60x160 mm cross-section for walls) and C24 grade timber. This wood is kiln-dried, four-side planed, and features chamfered edges. This rigorous technical processing removes moisture and fungal spores, while the smooth, chamfered surface causes flames to "slip" over the material, drastically increasing the structure's fire resistance.

6. How fast is the house built, and what does the Premium Developer Standard include?
The assembly of prefabricated walls on the plot takes only 3 to 6 days, including the roof installation. The Premium Standard includes:

- Thermal XPS foundation slab
- Braas ceramic roof tiles (or alternative roofing)
- Airtight installation of energy-efficient triple-glazed windows and exterior doors
- Automatic garage door
- Floor screeds with water-based underfloor heating
- Fully routed electrical and plumbing installations
- Heat pump and HRV system
- Suspended drywall ceilings

7. Can construction costs increase during the build process?
No. We guarantee a fixed price established at the very beginning of the investment. There are no hidden surcharges or surprises during the construction phase. The first tranche of our payment schedule is used to contract and purchase materials in advance, which serves as your guarantee of budget stability, regardless of market inflation.

8. How do you test building airtightness, and why is it important?
We are fully transparent and absolutely confident in our build quality. Our houses are rigorously prepared for airtightness testing (Blower Door Test), which is standard practice in our target markets in Germany and Austria. The test objectively confirms the absence of air leaks, guaranteeing maximum heat retention within the building and ensuring peak performance of the HRV system.

9. How are cables and pipes routed to avoid damaging the insulation layers?
In our external walls, we utilize a dedicated, insulated service cavity mounted on a special timber batten framework. Conduits for electrical wiring and cutouts for junction boxes are prepared without penetrating the primary airtight layer (STEICO multi membra 5 vapor barrier membrane). This guarantees absolute system reliability, thermal barrier continuity, and long-term durability of the envelope.

10. What windows do you install, and what does "RAL warm installation" mean in practice?
Included in our standard price, we install high-end, energy-efficient triple-glazed Salamander Prestige PVC windows, achieving a thermal transmittance as low as Uw = 0.74 W/m²K. All windows, including large-scale HST sliding door systems, are installed using warm installation technology compliant with RAL guidelines. We utilize multi-functional expanding tapes, which completely eliminate wind penetration and thermal bridging around the window frames.

11. How does the durability of timber frame homes compare to masonry construction?
We build houses using premium materials that ensure structural longevity comparable to, and often exceeding, standard masonry homes. The key factors for this durability are:

- Selected, kiln-dried, and planed KVH and C24 certified structural timber.
- Diffusion-open technology that safely vents moisture outwards.
- Production that is rigorously controlled in factory conditions (BMF-RAL quality certification).

12. Can I use your services if I don't have a ready architectural design or a building permit?
Absolutely. We provide comprehensive support at every stage of the investment. We design houses from scratch, perfectly adapting them to the plot dimensions and your individual needs. We prepare the complete architectural and construction documentation, and, acting on a power of attorney, we handle the entire process of obtaining a legally binding building permit. We also offer ready-made floor plans and perform external design adaptations.

13. Can you hear footsteps from the upper floor in a timber house (floor acoustics)?
No, this problem does not exist in our builds. We utilize exceptionally rigid floor structures made of KVH timber (designed in accordance with European ULS and SLS structural norms), filled with 12 cm of wood wool insulation. Most importantly—unlike our competitors—we pour classic concrete screeds with water-based underfloor heating on the upper floor. This application provides fantastic vibration dampening and impact noise reduction.
